CS **Civil Suits · Promenix Softech**

Development status — plan vs actual

विकासाची सद्यस्थिती — ठरवलेलं काम विरुद्ध प्रत्यक्ष झालेलं काम

Status report · 1 / 5
As of 22 Oct 2026 · project day 3 of the plan


PHASE 1 — DEMO
73%
8 of 13 items done · rest waiting on inputs


WHOLE ROADMAP
61%
19 done · 12 partly · 41 items

AUTOMATED CHECKS
280
186 unit tests + 94 database security checks

LIVE
Yes
Website + Android app · 18 DB migrations · 22 commits

PROGRESS BY PHASE (DONE = 1, PARTLY DONE = ½)

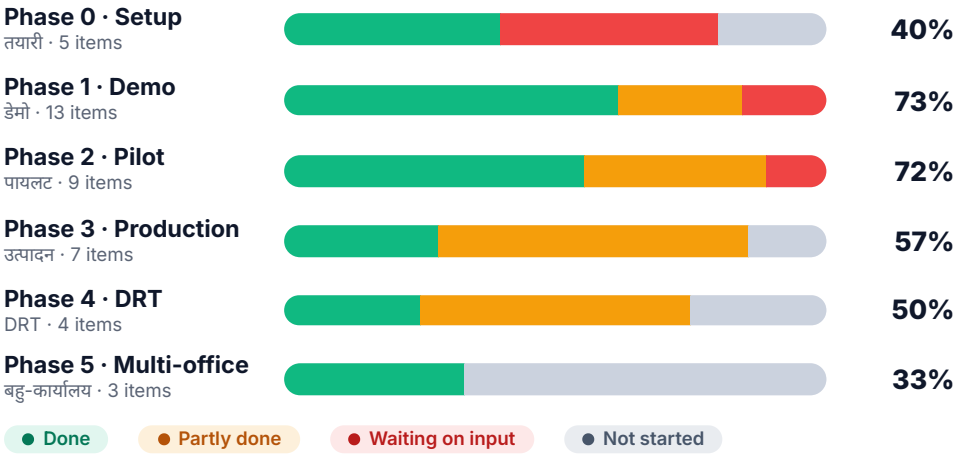

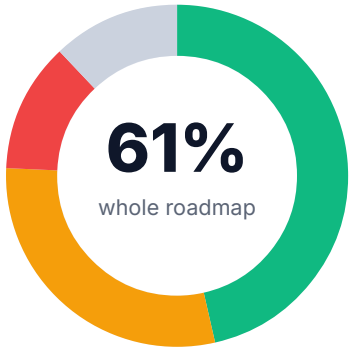

HEADLINE

Phase 1 (demo) is 73% complete — the full journey from case opening to an approved plaint works in the live app. What is left in Phase 1 is **waiting on inputs** (gazette text, Marathi legal terms, a server for PDF/A), not on development.


Donut = all 41 plan items across Phases 0–5. Two AI features are built and tested against a mock but await their first live run on the website.

Source: docs/plan.md (roadmap D) and docs/STATUS.md · live site civil-suits-manoj-76ab.vercel.app

Timeline — plan vs actual

वेळापत्रक — ठरवलेला कालावधी आणि प्रत्यक्ष प्रगती

Week 0 = 20 Oct 2026 (project start)

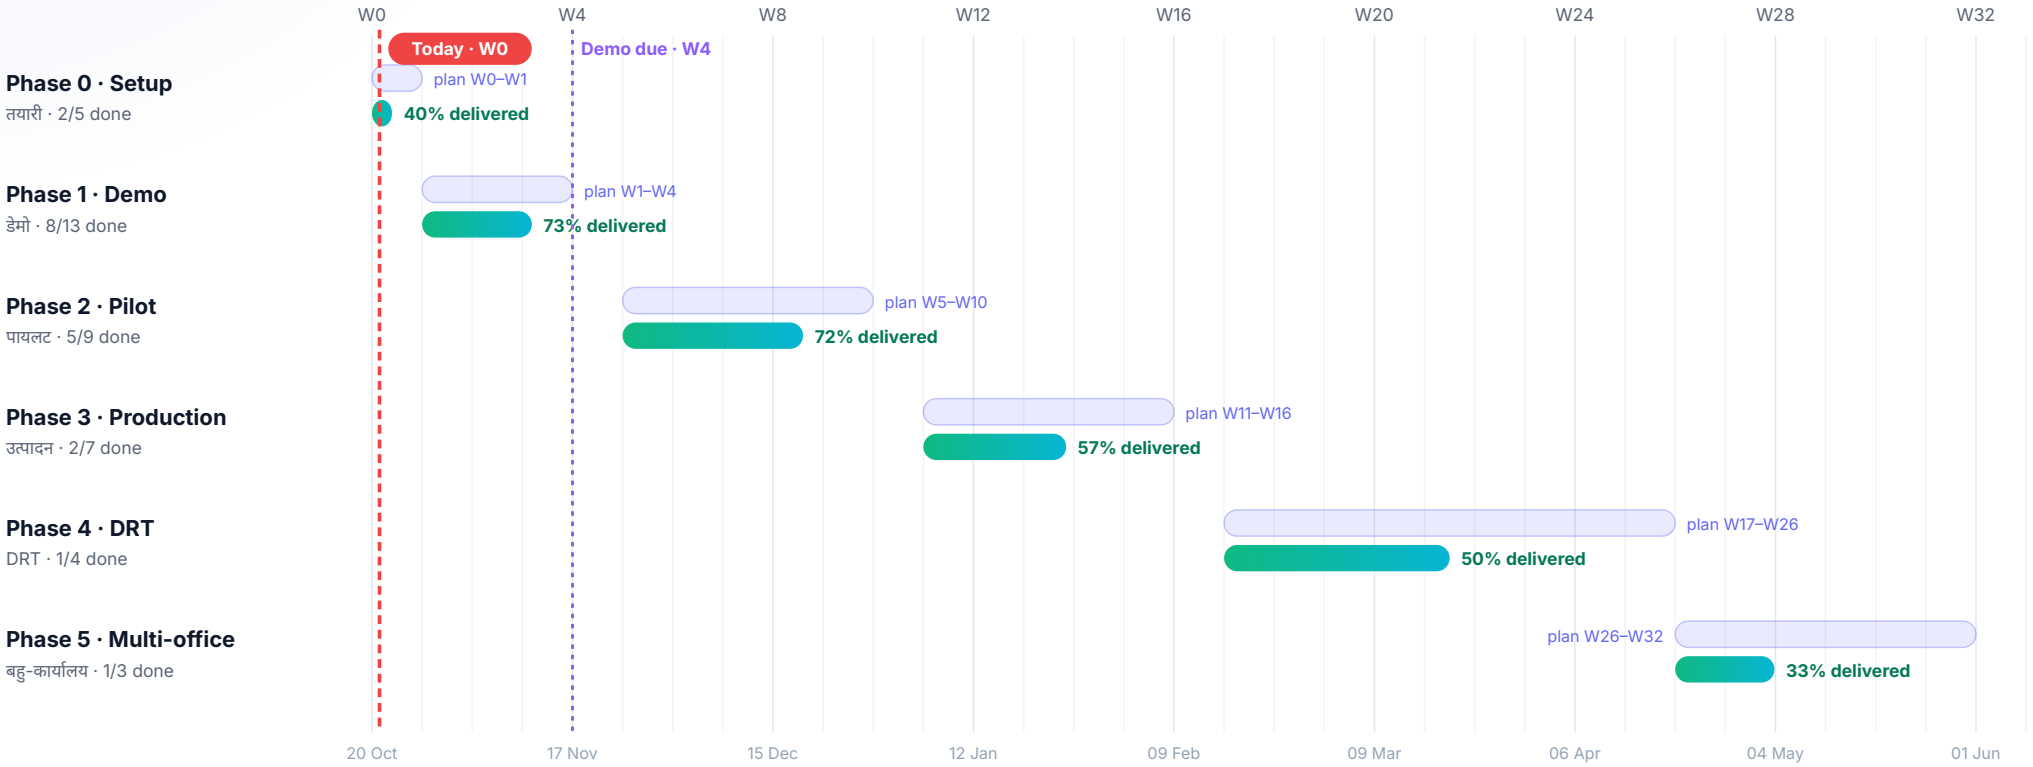

Light bar = planned window from the roadmap. Solid bar = share of that phase's items already delivered. Work on Phases 2–5 started early where it was cheap to do alongside Phase 1 (approvals, audit, 12A stage, calculators, multi-tenant model). The Phase 1 demo was planned for the end of week 4 (≈ 17 Nov 2026).

Dates are planning targets; Phases 3–5 depend on the pilot decision and paid infrastructure.


Where the work stands — by area

क्षेत्रानुसार प्रगती

ITEMS PER AREA



QUALITY AND SAFETY EVIDENCE

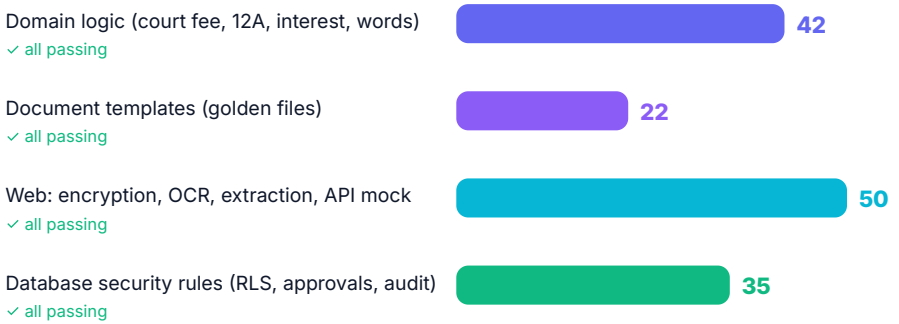

DELIVERED BEYOND THE PLAN

- Frosted-glass interface with light/dark mode and hover effects
- Android app (APK) and installable web app for the Field role
- Audit-chain verification page that detects tampering
- Security fix: only an admin can change who drafts or approves a case
- Field-level encryption for OCR text, account numbers and extracted values

Tests run on every change; database rules are tested against a real Postgres.

Plan items — Phase 0, 1 and 2

ठरवलेली कामे आणि त्यांची प्रत्यक्ष स्थिती

PHASE 0 · SETUP

1	**Repository, CI and AI-assisted dev setup** Rules, hooks, agents, skills	Platform	Done
2	**Synthetic demo data** 10 cases + scanned loan-file generator	Platform	Done
3	**NDA signed** Client	Client	Waiting
4	**Redacted sample file + format preferences** Client, after NDA	Client	Waiting
5	**Time-and-motion study (3–5 suits)** With client clerk	Client	Not started

PHASE 2 · PILOT

1	**Bulk upload, page classification, case split** Built and tested; needs VPS	AI	Partly
2	**Bank-specific templates (SBI, UBI, PNB, BoM)** Generic templates; bank variants pending	Documents	Partly
3	**Maker–checker approvals (DB-enforced)**	Workflow	Done
4	**Audit trail, viewer, tamper check**	Platform	Done
5	**Tasks + Field mobile view** Assign, phone view, photo proof	Field	Done
6	**E-filing bundle (bookmarks, file names)** Built and tested; needs VPS	E-filing	Partly
7	**Court-fee and interest calculators**	Workflow	Done
8	**12A mediation stage + notice dispatch**	Workflow	Done
9	**Paid infrastructure (Mumbai DB, Vercel Pro, VPS)** Owner decision	Platform	Waiting

PHASE 1 · DEMO

1	**Login and four roles (row-level security)** MFA deferred by owner	Platform	Done
2	**Open case, assign drafter + approver**	Workflow	Done
3	**Upload scans to private storage**	Workflow	Done
4	**OCR — Sarvam Document Intelligence** Built; first live run pending	AI	Partly
5	**Field extraction + verification screen** Built; first live run pending	AI	Partly
6	**Demand notice** Legal paragraphs flagged	Documents	Done
7	**Plaint (ordinary / O.XXXVII / commercial)** Legal paragraphs flagged	Documents	Done
8	**Vakalatnama** Stamp amounts to confirm	Documents	Done
9	**Affidavit / statement of truth** Declaration text pending	Documents	Done
10	**Bankers' Books Evidence Act 2026 certificate** Gazette text	Documents	Waiting
11	**Marathi versions** Legal glossary	Documents	Waiting
12	**PDF/A output** Worker built and tested; needs VPS	E-filing	Partly
13	**Role dashboards**	Workflow	Done

Phases 3–5 (billing, operations, DRT, multi-office) are listed in the plan; early items are counted on page 1.

What is needed to finish Phase 1 — and what comes next

Phase 1 पूर्ण करण्यासाठी काय लागेल, आणि पुढचे टप्पे

WAITING ON INPUT (OWNER · ADVOCATE · CLIENT)

Gazette text of the Bankers' Books Evidence Act 2026 schedules — Advocate / owner

Unblocks the bank-statement certificate for every case type.

Confirmed Marathi legal terms (glossary items marked †) — Advocate

Unblocks Marathi notices and pleadings.

Advocate's text for the [[LEGAL_REVIEW]] paragraphs — Advocate

Plaint averments, verification / statement-of-truth declarations, vakalatnama powers, stamp amounts.

A small VPS for the document worker — Owner

The worker is built and tested; a VPS turns on PDF/A, the e-filing bundle and case ZIPs.

Paid Mumbai database + Vercel Pro — Owner

Required before real bank data and before billing the client.

Signed NDA and one redacted sample file — Client

Real formats to match; time study for the ROI case.

BUILT, FIRST LIVE CHECK PENDING

OCR on a real scan (Sarvam)

Tested against a local mock of the API; the build sandbox cannot reach api.sarvam.ai. One upload on the live site confirms it.

Field extraction on a real scan

Same as above; confidence format to be confirmed on the first real result.

Document worker (PDF/A, bundle, ZIP, bulk upload)

Built and tested with the real converters; runs once a VPS is set up.

Billing, export, bulk upload, field tasks on the demo DB

Applied to the demo DB; first real run needs the worker on a VPS.

NEXT DEVELOPMENT STEPS (NO EXTERNAL DEPENDENCY)

Interest up to filing date

Add accrued interest to the claim in code once the advocate confirms simple vs compound per sanction terms.

Claude page classification (optional)

The in-code classifier works today; Claude Haiku can be added once an Anthropic key is set.

Bank-specific templates

SBI / UBI / PNB / BoM variants, once the advocate sends the office formats.

MFA for admin and approver

Deferred on the owner's instruction (20 Oct 2026); planned before real client data.

Before real bank data: Mumbai-region paid database, rotated keys, MFA, VAPT, signed NDA.
